# Preliminary Schedule - Solar

Exhibit J

| ID | Task Name | Duration | Start | Finish |
|---|---|---|---|---|
| 1 | City of Patterson - Solar Project | 394 days | Mon 3/30/26 | Thu 9/30/27 |
| 2 | City Hall | 150 days | Mon 3/30/26 | Fri 10/23/26 |
| 3 | Envelope-Base Re-roofing | 53 days | Mon 5/11/26 | Wed 7/22/26 |
| 4 | Submittal/Design Approval | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 5 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 6 | Plans Approval/Permit Issuance | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 7 | Installation Rooftop | 60 days | Wed 7/1/26 | Tue 9/22/26 |
| 8 | Punchlist/PTO Issuance | 23 days | Wed 9/23/26 | Fri 10/23/26 |
| 9 | Fire Station #1 | 200 days | Mon 3/30/26 | Fri 1/1/27 |
| 10 | Envelope-Base Re-roofing | 53 days | Thu 7/23/26 | Mon 10/5/26 |
| 11 | Submittal/Design Approval | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 12 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 13 | Plans Approval/Permit Issuance | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 14 | Installation Rooftop | 50 days | Wed 9/23/26 | Tue 12/1/26 |
| 15 | Punchlist/PTO Issuance | 23 days | Wed 12/2/26 | Fri 1/1/27 |
| 16 | Fire Station #2 | 260 days | Mon 3/30/26 | Fri 3/26/27 |
| 17 | Submittal/Design Approval | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 18 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 19 | Plans Approval/Permit Issuance | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 20 | Installation Rooftop | 60 days | Wed 12/2/26 | Tue 2/23/27 |
| 21 | Punchlist/PTO Issuance | 23 days | Wed 2/24/27 | Fri 3/26/27 |
| 22 | Old Corporate Yard | 320 days | Mon 3/30/26 | Fri 6/18/27 |
| 23 | Submittal/Design Approval | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 24 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 25 | Plans Approval/Permit Issuance | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 26 | Installation Rooftop | 60 days | Wed 2/24/27 | Tue 5/18/27 |
| 27 | Punchlist/PTO Issuance | 23 days | Wed 5/19/27 | Fri 6/18/27 |
| 28 | WWTP South | 163 days | Mon 3/30/26 | Wed 11/11/26 |
| 29 | Submittal/Design Approval | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 30 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 31 | Plans Approval | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 32 | Installation Groundmount Repair | 50 days | Mon 8/3/26 | Fri 10/9/26 |
| 33 | Punchlist/PTO Issuance | 23 days | Mon 10/12/26 | Wed 11/11/26 |
| 34 | Well 8 | 233 days | Mon 3/30/26 | Wed 2/17/27 |
| 35 | Submittal/Design Approval | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 36 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 37 | Plans Approval/Permit Issuance | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 38 | Installation Groundmount | 70 days | Mon 10/12/26 | Fri 1/15/27 |
| 39 | Punchlist/PTO Issuance | 23 days | Mon 1/18/27 | Wed 2/17/27 |
| 40 | Well 9 | 308 days | Mon 3/30/26 | Wed 6/2/27 |
| 41 | Submittal/Design Approval | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 42 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 43 | Plans Approval/Permit Issuance | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 44 | Installation Groundmount | 75 days | Mon 1/18/27 | Fri 4/30/27 |
| 45 | Punchlist/PTO Issuance | 23 days | Mon 5/3/27 | Wed 6/2/27 |
| 46 | Well 11 | 394 days | Mon 3/30/26 | Thu 9/30/27 |
| 47 | Submittal/Design Review | 13 days | Mon 3/30/26 | Wed 4/15/26 |
| 48 | Engineering | 40 days | Thu 4/16/26 | Wed 6/10/26 |
| 49 | Plans Approval/Permit Issuance | 14 days | Thu 6/11/26 | Tue 6/30/26 |
| 50 | Installation Groundmount | 86 days | Mon 5/3/27 | Mon 8/30/27 |
| 51 | Punchlist/PTO Issuance | 23 days | Tue 8/31/27 | Thu 9/30/27 |

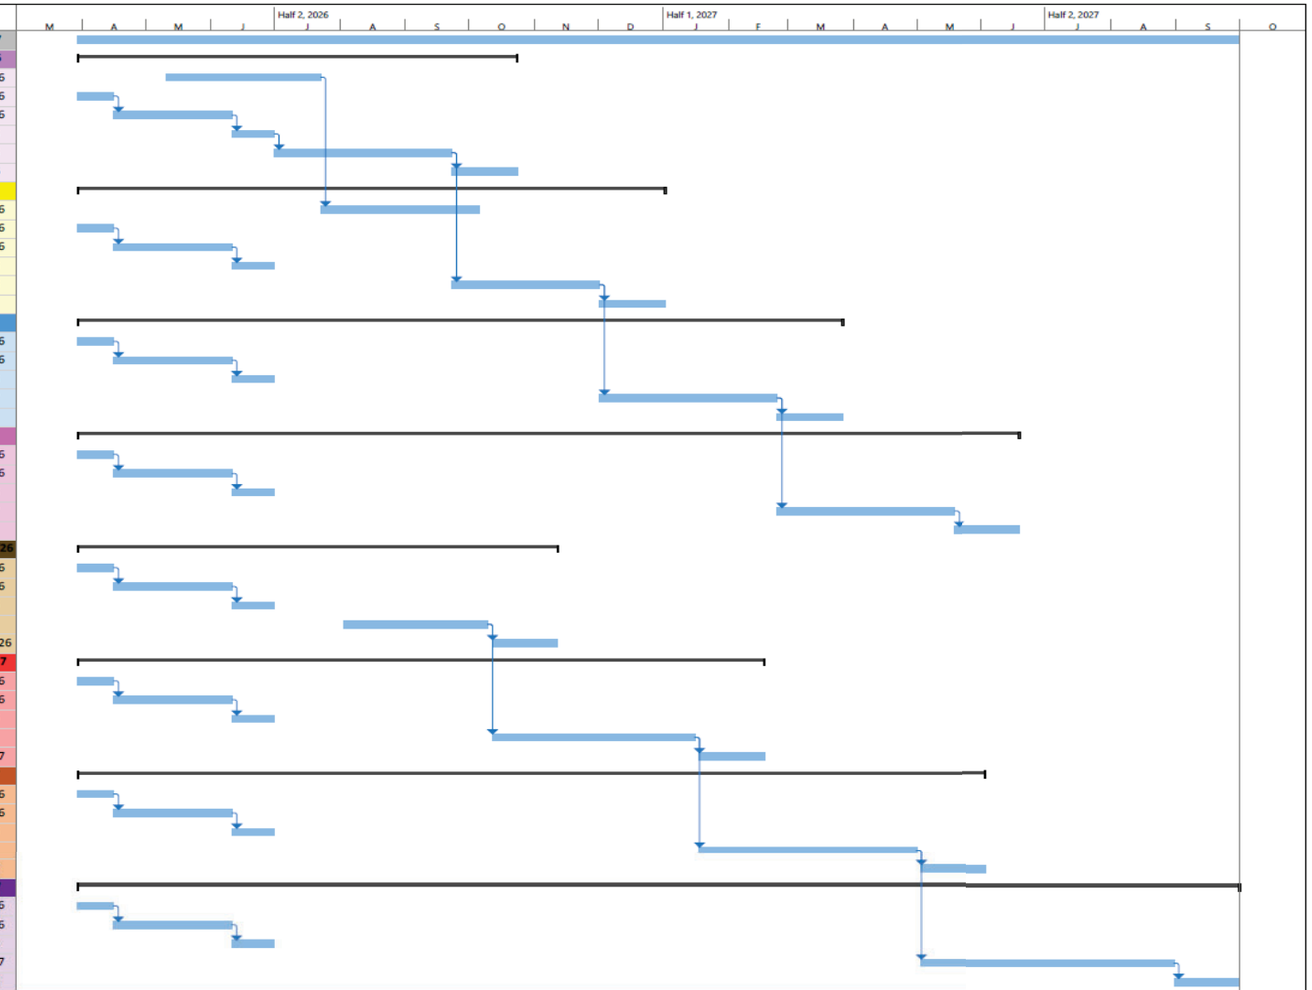


Project: City of Patterson-Solar
Date: Thu 2/12/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

Page 1
