Preliminary Schedule – Energy Infrastructure

Exhibit I

ID	Task Name	Duration	Start	Finish
1	City of Patterson - Energy Project	394 days	Mon 3/30/26	Thu 9/30/27
2	Submittal Approvals	45 days	Mon 3/30/26	Fri 5/29/26
3	Lighting Submittals	24 days	Mon 3/30/26	Thu 4/30/26
4	Transformer Submittals	40 days	Mon 3/30/26	Fri 5/22/26
5	HVAC/Controls Submittals	45 days	Mon 3/30/26	Fri 5/29/26
6	Aquatic Center	28 days	Mon 5/4/26	Wed 6/10/26
7	Interior Lighting	8 days	Mon 5/4/26	Wed 5/13/26
8	HVAC Controls (2 Units)	8 days	Mon 6/1/26	Wed 6/10/26
9	City Hall	120 days	Thu 5/14/26	Wed 10/28/26
10	Interior Lighting	17 days	Thu 5/14/26	Fri 6/5/26
11	Exterior Lighting	7 days	Mon 6/8/26	Tue 6/16/26
12	HVAC Replacements (5 Units)	42 days	Mon 8/24/26	Tue 10/20/26
13	HVAC Controls (2 Units)	6 days	Wed 10/21/26	Wed 10/28/26
14	Corporate Yard	143 days	Wed 6/17/26	Fri 1/1/27
15	Interior Lighting	9 days	Wed 6/17/26	Mon 6/29/26
16	Exterior Lighting	3 days	Tue 6/30/26	Thu 7/2/26
17	HVAC Replacements (3 Units)	38 days	Thu 10/29/26	Mon 12/21/26
18	HVAC Controls (3 Units)	9 days	Tue 12/22/26	Fri 1/1/27
19	Fire Station #1	149 days	Fri 7/3/26	Wed 1/27/27
20	Interior Lighting	10 days	Fri 7/3/26	Thu 7/16/26
21	HVAC Replacements (1 Unit)	10 days	Mon 1/4/27	Fri 1/15/27
22	HVAC Controls (3 Units)	8 days	Mon 1/18/27	Wed 1/27/27
23	Fire Station #2	193 days	Fri 7/17/26	Tue 4/13/27
24	Interior Lighting	4 days	Fri 7/17/26	Wed 7/22/26
25	Exterior Lighting	3 days	Thu 7/23/26	Mon 7/27/26
26	HVAC Replacements (4 Units)	45 days	Thu 1/28/27	Wed 3/31/27
27	HVAC Controls (3 Units)	9 days	Thu 4/1/27	Tue 4/13/27
28	Old Corporate Yard	4 days	Tue 7/28/26	Fri 7/31/26
29	Interior Lighting	4 days	Tue 7/28/26	Fri 7/31/26
30	Senior Center	196 days	Mon 8/3/26	Mon 5/3/27
31	Interior Lighting	10 days	Mon 8/3/26	Fri 8/14/26
32	Exterior Lighting	4 days	Mon 8/17/26	Thu 8/20/26
33	HVAC Controls (9 Units)	14 days	Wed 4/14/27	Mon 5/3/27
34	WWTP South	14 days	Fri 8/21/26	Wed 9/9/26
35	Interior Lighting	10 days	Fri 8/21/26	Thu 9/3/26
36	Transformer Replacement (1)	4 days	Fri 9/4/26	Wed 9/9/26

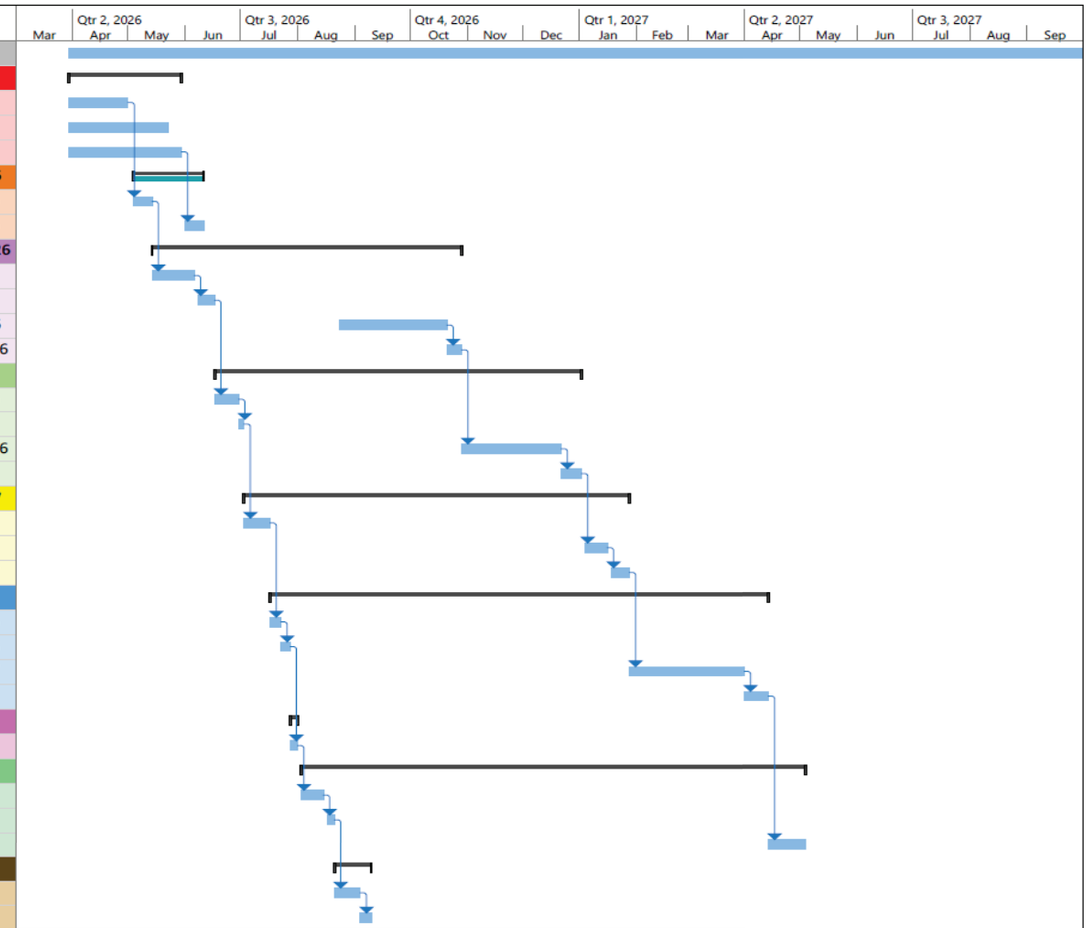

Project: City of Patterson-Energ
Date: Thu 2/12/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

Page 1
